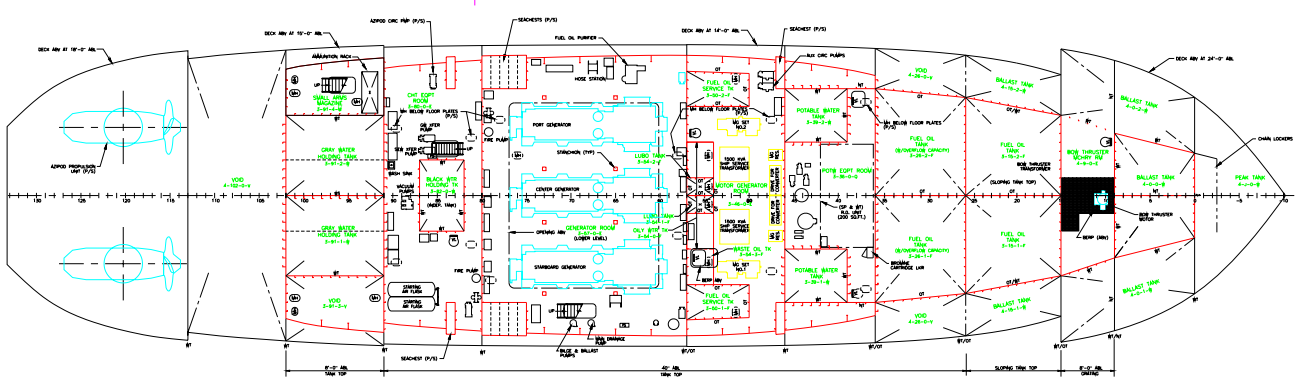

REVISIONS

SYM	NO.	DESCRIPTION	DATE	APPROVED
MJP,STC	C	1) ADDED SMOKE DOORS AT FR. 60 & 87 IN MAIN DECK PASS PER ECP-20A. ALSO ADDED PASS 1-80-2-1 & CHANGED DESIGNATION OF PASS 1-80-2-1 TO 1-80-2-2.		
KTP		2) ADDED DOOR FROM BHD FR. 47.2 TO SIDE OF SURGE WC,SH 2-2-48-1-L, SHIFTED SURGE HEADS OUTBD 5".		
TS,TSC SEN		3) INCREASED LENGTH OF ACCOMMODATION LADDER AND SHIFTED MIDSHIP 20 CM. GUN MOUNT FWD TO FR. 49.		
CDS,MAC TTO		4) RELOCATED D1 LEVEL HATCH INTO AZIPOD RM FROM STBD TO PORT FOR IMPROVED ACCESS AND LINE HANDLING.		
MAC		5) CHANGED STBD BHD IN MED TRTMT RM. WAS 2" JONER, NOW STEEL WITH 1" JONER LINER. CHANGED PER NOISE CONCERNS.		
PT,STP		6) RAISED TOP OF FAN RM 05-57-0-O 6", TO 75'-6" ABL PER DESIGN HISTORY 103.		
VAR		7) REVISED EQUIPMENT IN VARIOUS SPACES TO AGREE WITH SAFETY MANAGEMENTS PER DESIGN DEVELOPMENT.		
SAE		8) DELETED SANITARIES BHD IN ELEC SHOP AT FR. 77 PER DESIGN HISTORY 103.		
MAL,BAD		9) RELOCATED ACCESS DOORS INTO TRANSFORMER ROOMS 2-36-1-O & 2-36-2-O FROM FR. 37 TO BHD 46. DOORS ARE NOW BT AND SPACES ARE VITAL.		
SSC,SSP TTR,TSC		10) DELETED GRAY WATER SHORE TIE AT FR. 100 AND COMBINED GW WITH SEWAGE CONNECTION AT FR. 86.		
VAR		11) ADDED FIRE STATIONS AND LABELED AFFF REELS THROUGH OUT SHIP.		
LH		12) ADDED LIST OF ABBREVIATIONS.		
VAR		13) ADDED SMOKE BLANKET STOWAGES THROUGHOUT TO SUIT DESIGN DEVELOPMENT.		
SAF		14) RELOCATED BERP IN MACH SHOP AFT AND GRINDER FWD TO PROVIDE CLEAR REMOVAL PATH.		
WL,STB		15) ADDED LOUVERS FOR GEN RM AND AUX/EMER GEN RM.		
VAR		16) ADDED SAFETY RAILS AND OPENINGS IN PLATFORM DECK. BOW THRUSTER RM, GEN RM AND AZIPOD SPACE.		
MAC		17) CHANGED HINGE ORIENTATION OF DOOR INTO EXERCISE RM.		
TRS,ESC MAC,TSC		18) RELOCATED FWD & AFT CAPSTAN CONTROL STATIONS TO IMPROVE LINE OF SIGHT.		
MJP,SAC		19) ADDED INERT GAS CYLINDER STBD IN DC SHOP AND DECK GEAR LOCKER.		
VAR		20) CORRECTED LABELING AND TYPOGRAPHICAL ERRORS THROUGH OUT SHIP.		
AL		21) ADDED ELECTRIC BELL.		
S/G		22) ADDED BERP IN MAIN DECK PASSAGE FOR EQPT REMOVAL.		
TRS,ESC MAC,TSC		23) DELETED P/S MOORING WINCH CONT STATIONS AND ADDED SINGLE STATIONS ON CL. TETHERED MOORING CONTROLS PLUG INTO CL STATIONS.		
SSC,TSC SEN,MAC		24) ADDED VERTICAL LADDER ACCESS TO FOCSLE AT FR.11 STBD.		
TS,TPR SEN		25) RELOCATED BOW THRUSTER AND MOTOR PER DESIGN DEVELOPMENT.		
S/W		26) CHANGED SURGE BEARING FROM ENLISTED SIZE TO CPO SIZE PER CG REQUEST (REA-8).		
MAP		27) RELOCATED REFR CONTROL PANEL INTO PROV STRM ON REFR, AND ADDED REFR ALARM PANEL IN MESS ADJACENT TO GALLEY ENTRANCE.		
VAR		28) ADDED MAN HOLES THROUGHOUT PER DESIGN DEVELOPMENT.		
SSC,S/W SEN		29) DELETED OPENINGS IN PLT DK FR.9-12 AND ADDED PLATFORM DECK PER CG REQUEST. PLATFORM DK FR. 9-15 IS NOW WATERTIGHT.		
MAC		30) CHANGED SIZE OF DECK HOUSE WINDOWS, FROM 32"x40" TO 29"x36".		
MAL SEN		31) PLATFORM DECK FR. 46-57 IS NOW WATERTIGHT PER CG REQUEST. RELOCATED BERP FROM FR. 48 TO 56 AND RESIZED. ITEMS 7, 9, 10-12, 15-21 CHANGED PER CG COMMENTS LTR SER 801-GOA-00568 DTD 16 APR 03.		
			6/23/04	R.HANLEN
MAC,MAP	11	1) REMOVED COMPUTER WORK STATIONS FROM DC SHOP, MACH SHOP & 02 STRM PER ECP-23.		
SAG		2) DELETED STANCHION FR. 102 IN ENL MESS.		
SSE		3) DELETED CO2 LKR 1-46-1-A AND RENAMED PASSAGE 1-49-1-A TO 1-46-1-A.		
S,SS,TTC		4) DELETED TOILETS AND SINKS ON AFT WEATHER DECK FR. 122 PER CG REQUEST.		
MLA,AC		5) DELETED PORT ANCHOR CONTROL STATION, ONLY ONE STATION IS PROVIDED.		
STC,TTW LAP		6) RELOCATED 20 CAL GUN MOUNTS FROM FR. 130 TO FR. 128 P/S AND DELETED RAISED GRATING PLATFORMS. REDESIGNATED ALL .50 CAL MOUNTS AS MGAD GUNS.		
MAP,SAE		7) REARRANGED SHOP EQPT IN MACH SHOP AND ADDED AFFF RING STBD. ALL PASS 1-47-2-1-L, ALL PER DESIGN DEVELOPMENT.		
SAF		8) ADDED WALKWAYS ON PLT DK FR.9-12 PORT, CENTER & STBD ON PASS 4 TO AGREE WITH SHEET 3.		
VAR		9) CHANGED THE FOLLOWING SPACES FROM "O" DESIGNATORS TO "E" PER CG REQUEST: CHT EQPT RM. TRANSFORMER RMS (2). MOTOR GEN RM. PROP TRANSFORMER RMS (2). MAIN PROPULSION MACH RM. AZIPOD SPACE. SHAFT RM.		
TRS,ESC MAC,MAN		10) ADDED AFT CONNING STATION 03-93-1-C, RADAR & SEARCH LIGHT. ADDED EXTERIOR EMD RADIATOR 02 WEATHER DECK. ALL PER ECP-20.		
MAC		11) DELETED ELEV/C SHOP 03-72-2-O AND COMBINED ELEV SHOP WITH MACH RM 05-69-2-O. CHANGED ALL 03-72-0-O TO 03-72-1-O PER DESIGN DEVELOPMENT.		
CDS,STC STP,STC	12)	CONSIDERED VOID 4-15-0-O INTO BALLAST TKS 04-15-1-W & 2-15-1-W. ADDED MAINTENANCE CORRIDORS 2-15-3-O & 2-15-4-O WITH ACCESS DOORS IN BHD 26. ALL TO SUIT ECP-30.		
MJP,S/W		13) ADDED SCBA ARMACK STBD IN VICINITY OF BOTH REPAIR STATIONS. DELETED SCBA STBD CABINETS AND ADDED STANLEY TOOL CHEST LOCKER 3 ALL TO SUIT DESIGN DEVELOPMENT.		
TP,TP SEN		14) RELOCATED LIFE RAFTS FROM FANTAIL TO AMIDSHIPS PER ECP-20.		
S/W,TC		15) REARRANGED ENG/LOG OFFICE AND ADDED DIAGNOSTICS CUBICLE. ALL TO SUIT ECP-11.		
VAR		16) RELEASED RESERVATIONS 1 & 2.		
MAL,BAD		17) CHANGED DOOR SWINGS WEA DOORS 01 LVL FR. 76 P/S.		
MAP		18) ADDED METAL SHORING STBD AT FR107 CL MAIN DECK PER DESIGN DEVELOPMENT.		
SSJ,TC SEN,MAN		19) CHANGED OTS SAR BOAT FROM ZODIAC TO SILVERSHIPS MODEL. RELOCATED INBD. ALL PER REA-14.		
SAC		20) ADDED MAINTENANCE WALKWAYS FIRST PLT GENERATOR RM.		
AVS		21) REARRANGED SHIP TRAINING RM TO ACCOMMODATE SIMULATOR PER CG.		
SSC,SAP		22) DELETED HYDR OIL TK IN AZIPOD SPACE FR.125 (S).		
			2/2/04	R.HANLEN
